FOUND POINTS

SEC	PT	COORDINATES NORTH	COORDINATES EAST	DESCRIPTION	RECORDED BK	RECORDED OF	RECORDED PG
23	1	154,282.20	2,394,444.87	USFS 3 1/4"A.C. ON 2 1/2"A.P. IN M.O.R.	6	R/S	121
23	2	154,406.24	2,397,115.81	3/4" I.P. L.S. 2846	3	R/S	148
--	--	153,655.46	2,396,678.34	CM 5.29R	--	--	--
--	--	154,258.67	2,396,425.28	CM 5.37	--	--	--
--	--	154,655.32	2,395,612.57	CM 5.55R	--	--	--
--	--	155,126.71	2,395,176.50	CM 5.67	--	--	--

LEGEND

- △ CALTRANS CONTROL LINE MONUMENT
- □ FOUND R/W MONUMENT
- ■ SET 3/4" REBAR W/ALUM. CAP STAMPED "CALTRANS"
- ∘ NO MONUMENT SET
- PROPERTY MONUMENT FOUND AS NOTED
- ● PROP. MON. FOUND AS NOTED AND REMOVED
- ◆ SECTION OR FRACTIONAL CORNER FOUND AS NOTED.
- ◇ SECTION OR FRACTIONAL CORNER NOT LOCATED.
- U.S.C.& G.S. TRIANGULATION STATION
- CALTRANS HORIZONTAL CONTROL STATION
- 36-9 SECTION-POINT No.

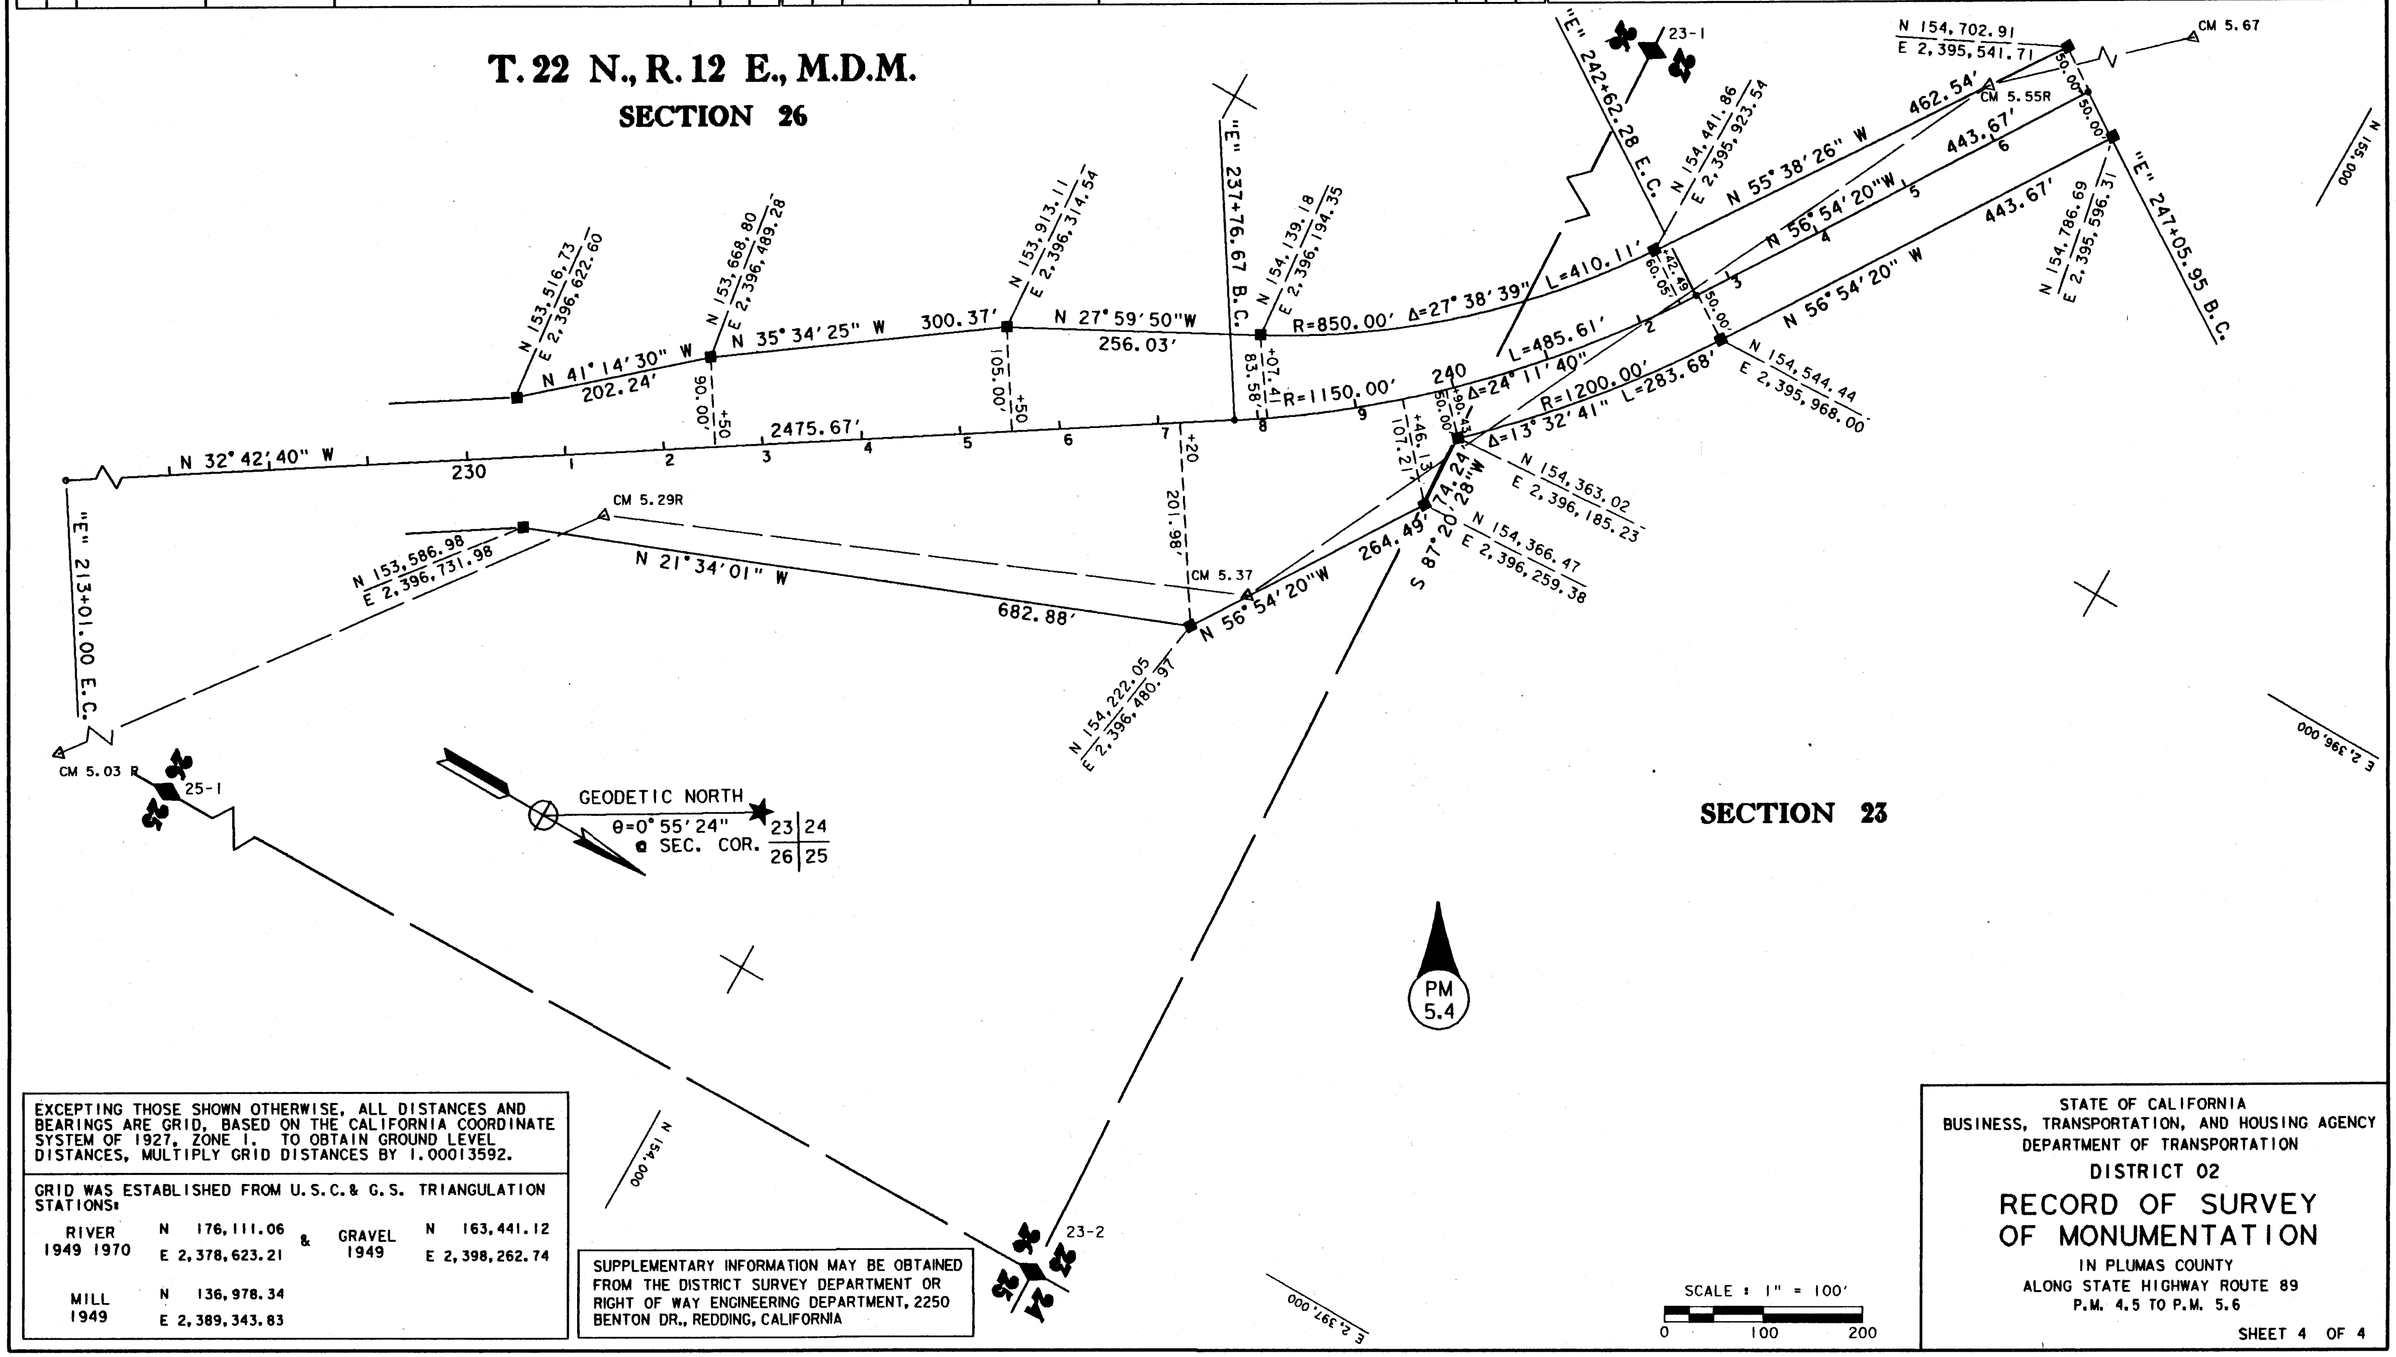

EXCEPTING THOSE SHOWN OTHERWISE, ALL DISTANCES AND BEARINGS ARE GRID, BASED ON THE CALIFORNIA COORDINATE SYSTEM OF 1927, ZONE 1. TO OBTAIN GROUND LEVEL DISTANCES, MULTIPLY GRID DISTANCES BY 1.00013592.

GRID WAS ESTABLISHED FROM U.S.C.& G.S. TRIANGULATION STATIONS:

RIVER 1949 1970	N 176,111.06 E 2,378,623.21	&	GRAVEL 1949	N 163,441.12 E 2,398,262.74
MILL 1949	N 136,978.34 E 2,389,343.83			

SUPPLEMENTARY INFORMATION MAY BE OBTAINED FROM THE DISTRICT SURVEY DEPARTMENT OR RIGHT OF WAY ENGINEERING DEPARTMENT, 2250 BENTON DR., REDDING, CALIFORNIA

STATE OF CALIFORNIA
BUSINESS, TRANSPORTATION, AND HOUSING AGENCY
DEPARTMENT OF TRANSPORTATION
DISTRICT 02

RECORD OF SURVEY OF MONUMENTATION

IN PLUMAS COUNTY
ALONG STATE HIGHWAY ROUTE 89
P.M. 4.5 TO P.M. 5.6

SHEET 4 OF 4
